



January 27, 2012

## **WEEKLY CONSTRUCTION PROGRESS UPDATE**


Jefferson Elementary School Modernization and Earthquake Repair  
DSA Project # 108342

### Notable Activities Achieved for the Week Ending January 27, 2012


1. Plaster Acrylic color coat on Plaster Buildings 1, 2 and 3
2. Installation of ceramic tile in Building 3 and 4 Restrooms
3. Conduit for Outside Lighting under canopy
4. Starting of the install of Glazing (windows)

### Activities Scheduled for the Week Ending February 3, 2012


1. Installation of Classroom Cabinets
2. Installation of Window Glass
3. Ceramic Tile in Restrooms Building 5
4. Installation T Bar Grid for Ceilings in Classrooms

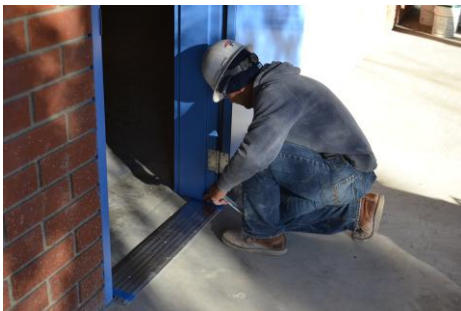

Installing thresholds for door Building 1

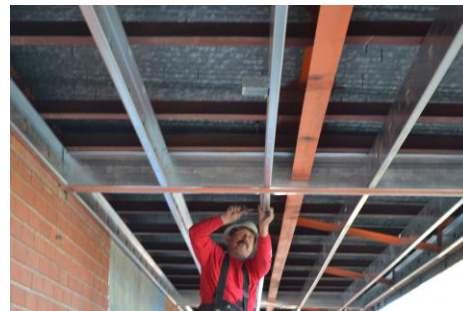

Installing conduit for outside lighting

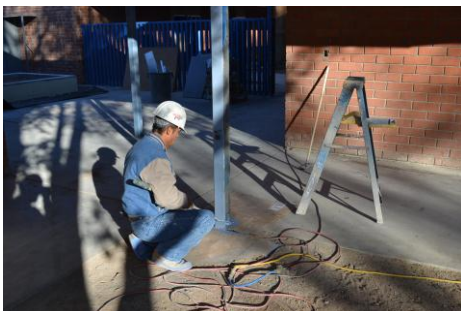

Painting Primer on Building Columns



Finished Exterior Plaster Building 2
